All aspects of this plan to be strictly adhered to

2x Cat C trees are to be removed (T's 3 & 4)

All other trees retained & protected

Access for works on the existing hard-standing.

No significant long-term impact to any retained trees is envisaged.

Protection measures will be put in place to safeguard the trees from any potential indirect impact, such as fencing off the canopies and RPA's and the use of temporary ground protection.

Fencing will create a Construction Exclusion Zone CEZ. No access for construction traffic or materials.

Existing boundary fencing will act a tree protection

Contractor's access on existing hard-standing at front of property

Site office/welfare outside any RPA

Unloading of materials away from retained trees onto existing hard-standing

No materials, mixing or washing out of tools within the RPA's

Washing out of tools and equipment not to be within 10m of any retained tree

All retained trees should be regularly monitored to assess health and potential


Arboriculturalist to visit site at regular intervals to check protection measures


Mitigation planting of 1x apple & 1x pear as shown

Temporary Ground Protection




Protective Fencing

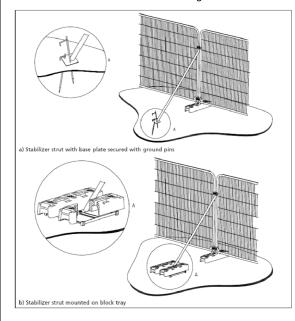


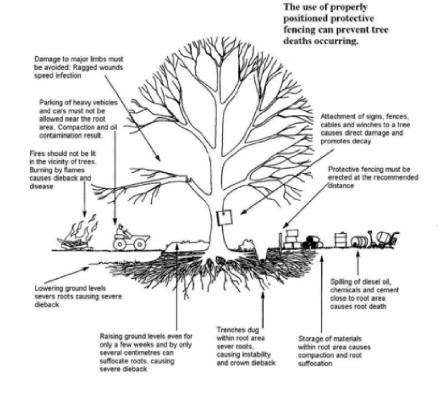

Common causes of Tree Death

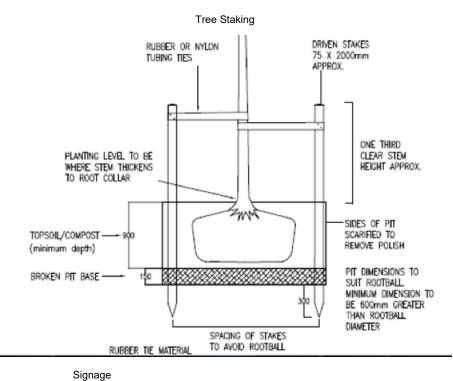



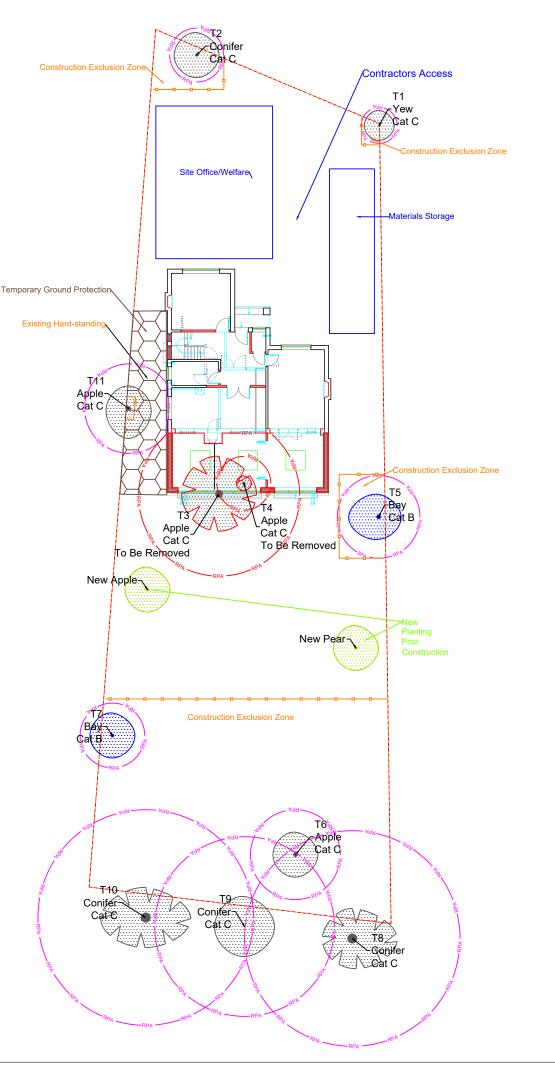

Tree Protection Plan showing surveyed trees & protection measures

Tree to be Retained

expectancy of at least 40





estimated remaining life expectancy of at least 10 years, or a stem diameter

Tree to be Removed









	No.	Revision/Issue	Date
	1		
	2		



info@central-londontreesurveys.com Tel: 0800 6891746

87 HANWORTH ROAD **HAMPTON TW12 3EA**

Project No 24141	Sheet 1 of 1		
Date 2024-07-11 07:52:33			
Scale			
1 to 200 at A3			
