Solum Twickenham

Rev P v9 - Summary Programme

Issue date:
15/03/2017

Line	Name	Duration	Start	Finish
1	**Possessions**		**09/04/2017**	**01/07/2019**
	Pre-Enabling Works			
2	Cable Delivery & Installation	3w 4d	20/03/2017	13/04/2017
3	**Enabling Works**	**18w 4d**	**03/04/2017**	**16/08/2017**
4	Foul Drainage	5w 3d	22/06/2017	31/07/2017
5	Trackside Cable Diversions	10w 1d	03/04/2017	16/06/2017
6	Temporary Ticket Office	11w 4d	22/05/2017	11/08/2017
7	Temp Relocate Platform Rail Services	8w 4d	16/06/2017	16/08/2017
8	Site Set Up	4w	05/06/2017	30/06/2017
9	**Station Podium**	**65w 4d**	**12/06/2017**	**05/10/2018**
10	Temporary Footbridge installation	4w	12/06/2017	07/07/2017
11	Existing High Level Walkway Removal	6w 4d	14/08/2017	29/09/2017
12	St Marys Terrace Enabling & Substructure	35w 4d	03/07/2017	23/03/2018
13	Platform 4/5 Extension	19w 4d	30/10/2017	29/03/2018
14	GL B7 PCC Edge Beams	3w	22/01/2018	09/02/2018
15	Block A - A18 to B6 Sub-structure	10w 3d	19/02/2018	04/05/2018
16	Install P.C.C. Beams		30/04/2018	14/05/2018
17	Podium Deck Construction Structural Infill	9w 3d	30/04/2018	06/07/2018
18	Lifts	15w 3d	14/05/2018	31/08/2018
19	Temp Footbridge Removal	1w	01/10/2018	05/10/2018
20	**Demolition & London Road Works**	**15w 4d**	**14/08/2017**	**01/12/2017**
21	Existing ticket office demolition	10w 4d	14/08/2017	27/10/2017
22	London Road Works	15w 4d	14/08/2017	01/12/2017
23	**Block A**	**74w**	**26/10/2017**	**03/05/2019**
24	Substructure	16w 2d	26/10/2017	02/03/2018
25	Superstructure	16w 4d	05/03/2018	04/07/2018
26	External Envelope	41w 1d	08/05/2018	07/03/2019
27	Internal Finishes & Services	37w 2d	14/05/2018	14/02/2019
28	External Works	20w	29/10/2018	29/03/2019
29	Test, Commission & Handover	15w 3d	14/01/2019	03/05/2019
30	Handover Marketing Suite		31/01/2019	31/01/2019
31	Handover Core 1		11/03/2019	11/03/2019
32	Handover Core 2		07/05/2019	07/05/2019
33	**Block B**	**89w 1d**	**24/11/2017**	**23/09/2019**
34	Substructure	18w 2d	24/11/2017	18/04/2018
35	Podium Deck Construction (As Above)	9w 3d	30/04/2018	06/07/2018
36	Completion of Structural Infill		11/06/2018	11/06/2018
37	Superstructure	26w 1d	12/06/2018	12/12/2018
38	External Envelope	47w 3d	23/07/2018	10/07/2019
39	Internal Finishes & Services	45w 1d	03/09/2018	02/08/2019
40	External Works/Public Realm	13w	27/02/2019	03/06/2019
41	Test, Commission & Handover	14w 3d	11/06/2019	20/09/2019
42	Handover Core 1		19/08/2019	19/08/2019
43	Handover Core 2		23/09/2019	23/09/2019
	New Ticket Office & Station Concourse			
44	Station Fit Out Shell & Core Inc M&E Infrastructure	23w 3d	24/09/2018	20/03/2019
45	External Works/Public Realm	12w 4d	27/11/2018	08/03/2019
46	Station Fitout By SWT, Gateline & Others	6w	23/01/2019	05/03/2019
47	Test & Commission Station	2w	21/03/2019	03/04/2019
48	New Ticket Office Operational		04/04/2019	04/04/2019
49	**Block C**	**53w**	**04/04/2019**	**01/05/2020**
50	Hoardings/Protection & TTO Removal	2w	04/04/2019	17/04/2019
51	Substructure	11w 2d	18/04/2019	11/07/2019
52	Superstructure	12w	08/07/2019	30/09/2019
53	External Envelope	23w 2d	17/09/2019	11/03/2020
54	Internal Finishes & Services	25w	17/09/2019	23/03/2020
55	External Works	16w 4d	20/12/2019	01/05/2020
56	Test, Commission & Handover	10w 3d	17/02/2020	01/05/2020
57	Handover Block C		01/05/2020	01/05/2020
58	Clear Site Set Up	4w	02/04/2020	01/05/2020

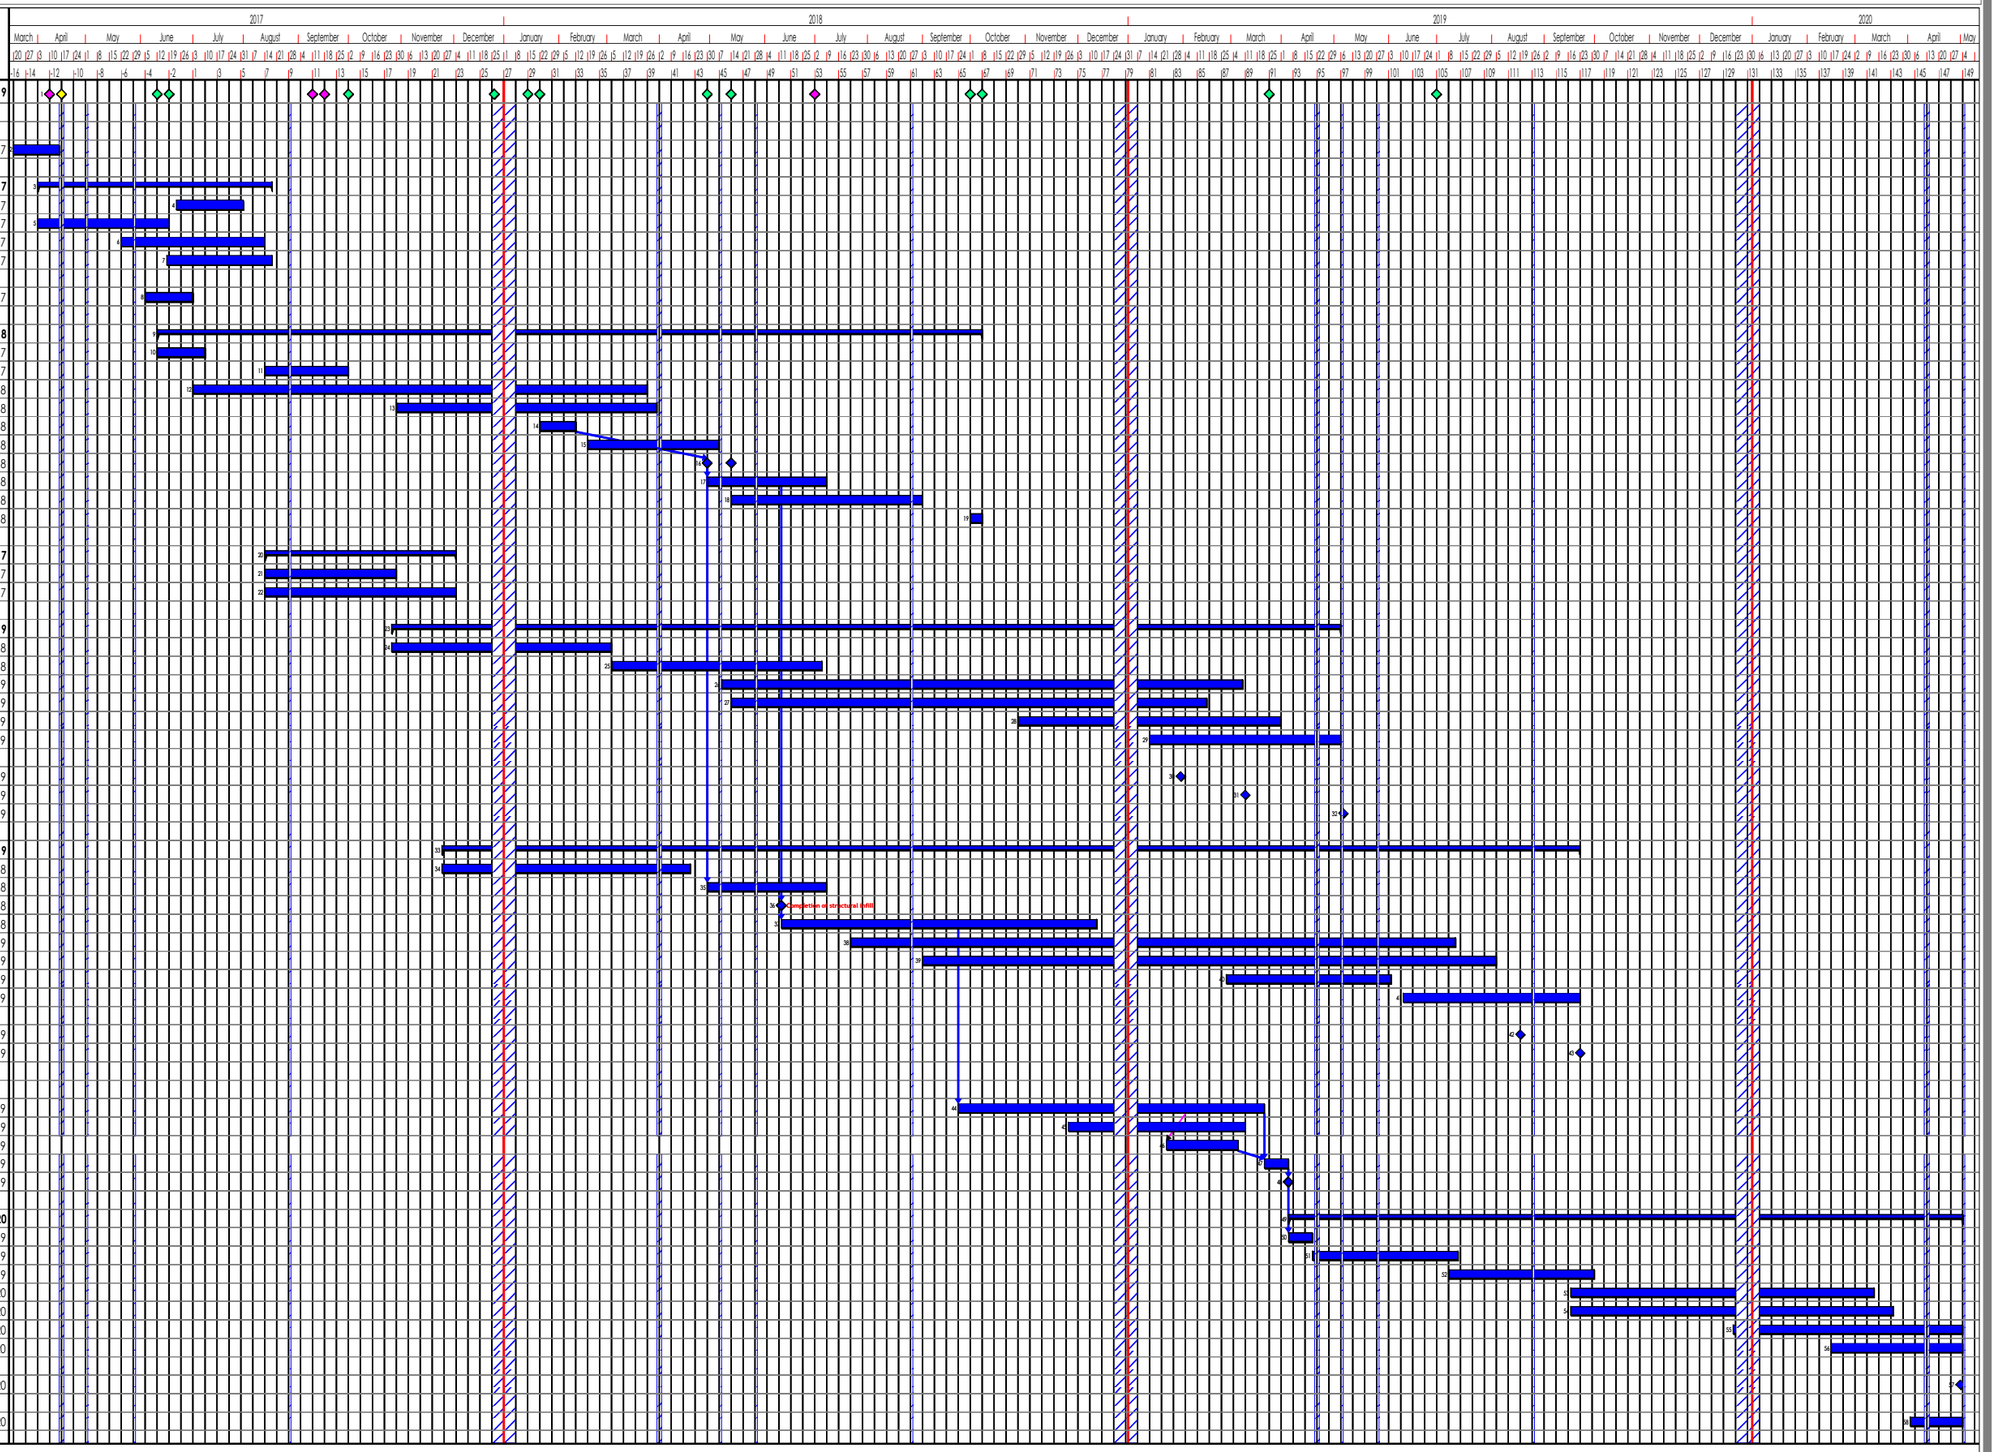

Key
28Hr Pos
76Hr Pos
52hr Pos
Construction

Drawn by:

Revision No. Pv9 Sum Rev 4

Dwg No. ASD/STW/004

Comments: Possessions Added

Project Ref. C:\Users\adridown\Documents\PowerProjectFiles\Solum Twickenham\Feb 17 Programme\Summary Programme 15th March 2017.pp
